




Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010											
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A									
Los Angeles City College																																																					
Total		2,787	05AUG00A	06JUL11	288,401,251	[Gantt bars for total project]																																															
101 Science and Technology Building																																																					
+ Pre-Design/Programming																																																					
		102	01APR02A	21AUG02A	0																																																
+ Project Design																																																					
		946	21OCT02A	03JUL06A	0																																																
+ Project DSA Review																																																					
		798	02SEP03A	18OCT06A	0																																																
+ Project Bid and Award																																																					
		97	04OCT06A	21FEB07	0																																																
+ Project Construction																																																					
		474	08MAR07	19JAN09	52,300,000																																																
+ Project Close-Out																																																					
		1,323	30SEP05A	16DEC10	0																																																
+ Commissioning																																																					
		2,259*	21OCT02A	26DEC08	0																																																
+ FF&E																																																					
		22	16DEC08	16JAN09	0																																																
+																																																					
		2,528*	01APR02A	02MAR09	0																																																
102 Family Life Science																																																					
+ Pre-Design/Programming																																																					
		977	16SEP02A	12JUL06A	0																																																
+ Project Design																																																					
		1,168	02DEC02A	29JUN07	0																																																
+ Project DSA Review																																																					
		192	17JUL07	16APR08	0																																																
+ Project Bid and Award																																																					
		1,315	30SEP05A	06DEC10	0																																																
+ Project Construction																																																					
		260	18FEB09	25FEB10	5,280,000																																																
+ Project Close-Out																																																					
		1,310	30SEP05A	29NOV10	0																																																
+ FF&E																																																					
		12	10FEB10	25FEB10	0																																																

Start Date 01AUG00  
 Finish Date 06JUL11  
 Data Date 31JAN07  
 Run Date 02MAR07 12:19

 Early Bar  
 Progress Bar  
 Critical Activity

017U

LACCD  
 Los Angeles City College  
 Campus Summary

Sheet 1 of 18

Date	Revision	Checked	Approved

Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010		
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A
+																																												
		2,781*	16SEP02A	27APR10	0																																							
106 Caesar Chavez - Admin Building																																												
+ Pre-Design/Programming																																												
		1,154	04SEP02A	13MAR07	0																																							
+ Project Design																																												
		1,117	07AUG03A	27DEC07	0																																							
+ Project DSA Review																																												
		151	08FEB08	10SEP08	0																																							
+ Project Bid and Award																																												
		1,372	30SEP05A	25FEB11	0																																							
+ Project Construction																																												
		230	10MAY10	05APR11	632,329																																							
+ Project Close-Out																																												
		55	06APR11	22JUN11	0																																							
+ FF&E																																												
		21	08MAR11	05APR11	0																																							
+																																												
		3,177*	04SEP02A	16MAY11	0																																							
107 Clausen Hall																																												
107.01 Clausen Hall - DSPS																																												
+ Project Bid and Award																																												
		48	07JUN02A	14AUG02A	0																																							
+ Project Construction																																												
		86	23SEP02A	22JAN03A	647,979																																							
+ Project Close-Out																																												
		449	24JAN03A	21OCT04A	0																																							
+																																												
		867*	07JUN02A	20OCT04A	0																																							
107.02 Clausen Hall Modernization																																												
+ Pre-Design/Programming																																												
		553	21OCT02A	15DEC04A	0																																							
+ Project Design																																												
		1,246	07AUG03A	27JUN08	0																																							
+ Project DSA Review																																												
		207	30JUN08	22APR09	0																																							
+ Project Bid and Award																																												
		1,315	30SEP05A	06DEC10	0																																							

Start Date 01AUG00  
Finish Date 06JUL11  
Data Date 31JAN07  
Run Date 02MAR07 12:19

Early Bar  
 Progress Bar  
 Critical Activity

017U  
LACCD  
Los Angeles City College  
Campus Summary

Date	Revision	Checked	Approved



Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010		
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A
<b>+ Project Close-Out</b>																																												
<b>+ FF&amp;E</b>																																												
<b>+</b>																																												
<b>110 Holmes Hall</b>																																												
<b>+ Project Design</b>																																												
<b>+ Project DSA Review</b>																																												
<b>+ Project Bid and Award</b>																																												
<b>+ Project Construction</b>																																												
<b>+ Project Close-Out</b>																																												
<b>+ FF&amp;E</b>																																												
<b>+</b>																																												
<b>111 Jefferson Hall</b>																																												
<b>+ Pre-Design/Programming</b>																																												
<b>+ Project Design</b>																																												
<b>+ Project DSA Review</b>																																												
<b>+ Project Bid and Award</b>																																												
<b>+ Project Construction</b>																																												
<b>+ Project Close-Out</b>																																												
<b>+ FF&amp;E</b>																																												

Start Date 01AUG00  
 Finish Date 06JUL11  
 Data Date 31JAN07  
 Run Date 02MAR07 12:19


Early Bar  
 Progress Bar  
 Critical Activity

017U




LACCD  
 Los Angeles City College  
 Campus Summary

Sheet 4 of 18

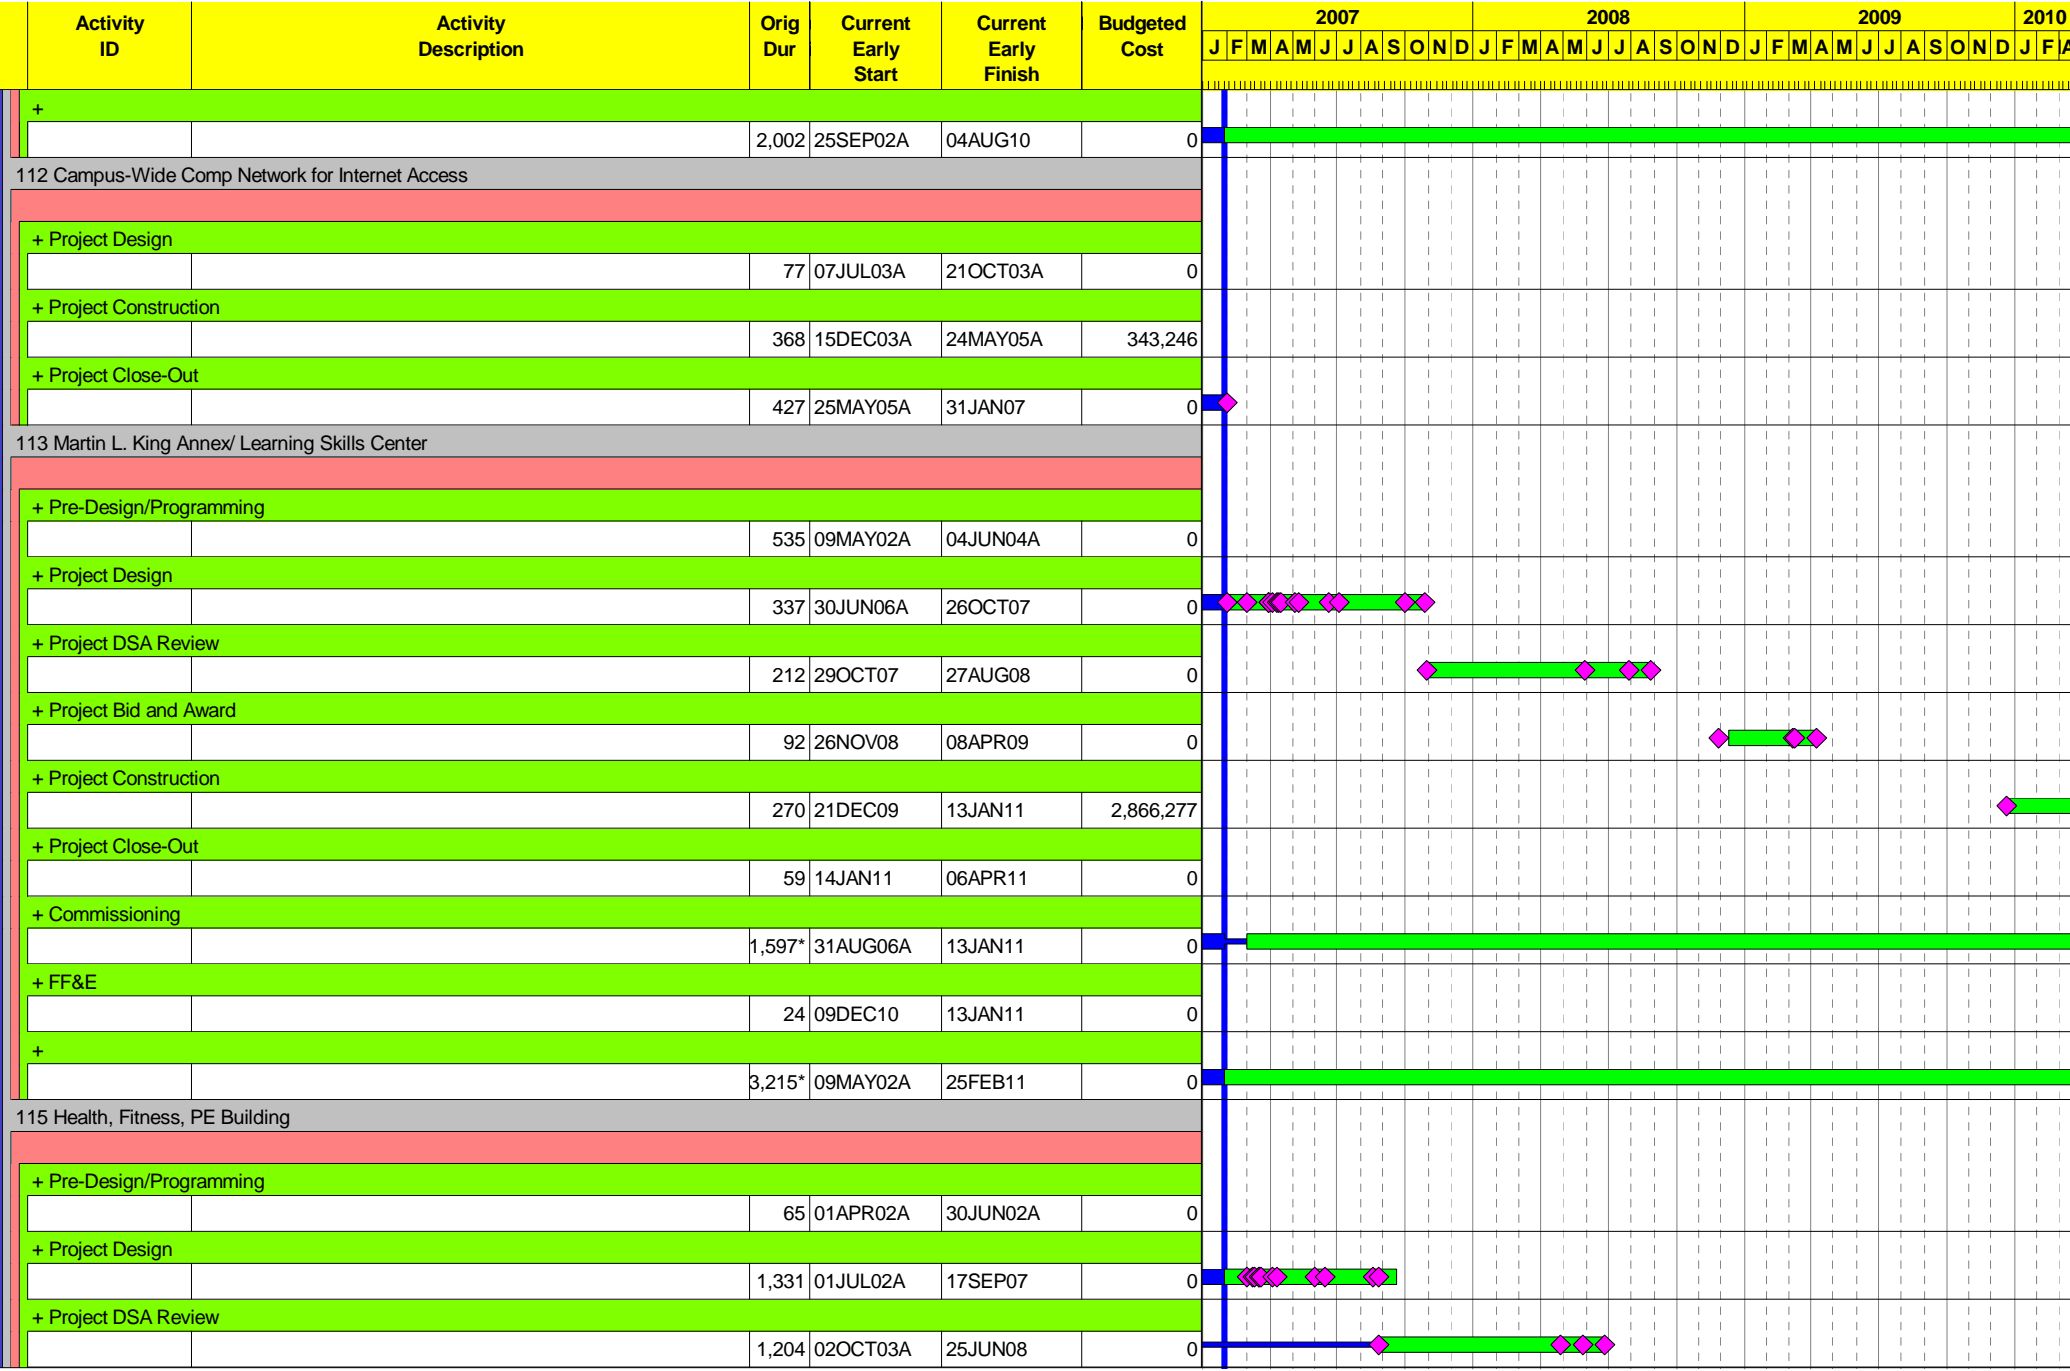Date	Revision	Checked	Approved



Start Date 01AUG00  
 Finish Date 06JUL11  
 Data Date 31JAN07  
 Run Date 02MAR07 12:19




 Early Bar  
 Progress Bar  
 Critical Activity

017U  
 LACCD  
 Los Angeles City College  
 Campus Summary

Date	Revision	Checked	Approved

Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010		
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A
+ Project Bid and Award																																												
		68	26JUN08	01OCT08	0																																							
+ Project Construction																																												
		242	02OCT08	15SEP09	32,002,255																																							
+ Project Close-Out																																												
		1,372	30SEP05A	25FEB11	0																																							
+ Commissioning																																												
		2,532*	11OCT02A	15SEP09	0																																							
+ FF&E																																												
		31	03AUG09	15SEP09	0																																							
+																																												
		1,954	01APR02A	25NOV09	0																																							
116/120/103: Parkg St./PE Bldg/Athletic Fld																																												
+ Pre-Design/Programming																																												
		65	01APR02A	30JUN02A	0																																							
+ Project Design																																												
		234	01JUL02A	27MAY03A	0																																							
+ Project DSA Review																																												
		310	28MAY03A	10AUG04A	0																																							
+ Project Bid and Award																																												
		183	20DEC04A	07SEP05A	0																																							
+ Project Construction																																												
		736	24OCT05A	29OCT07	52,370,000																																							
+ Project Close-Out																																												
		43	30OCT07	02JAN08	0																																							
+ FF&E																																												
		21	01OCT07	29OCT07	0																																							
+																																												
		2,103*	01APR02A	02JAN08	0																																							
117 Student Admissions Center-Terminated																																												
+ Pre-Design/Programming																																												
		59	01APR02A	20JUN02A	0																																							
+ Project Design																																												
		306	18APR02A	24JUN03A	963,263																																							
+ Project DSA Review																																												
		387	07FEB03A	09AUG04A	0																																							

Start Date 01AUG00  
 Finish Date 06JUL11  
 Data Date 31JAN07  
 Run Date 02MAR07 12:19

 Early Bar  
 Progress Bar  
 Critical Activity

017U

LACCD  
 Los Angeles City College  
 Campus Summary

Sheet 6 of 18

Date	Revision	Checked	Approved



Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010		
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A
+ Project Bid and Award																																												
		73	17JUL06A	26OCT06A	0																																							
+ Project Construction																																												
		370	11DEC06A	15DEC07	14,880,000																																							
+ Project Close-Out																																												
		71	17DEC07	26MAR08	0																																							
+																																												
		1,601*	01SEP03A	18JAN08	0																																							
Library Building - State Funded																																												
+ Pre-Design/Programming																																												
		495	30APR02A	30MAR04A	0																																							
+ Project Design																																												
		159	01APR04A	12NOV04A	0																																							
+ Project DSA Review																																												
		270	17NOV04A	12DEC05A	0																																							
+ Project Bid and Award																																												
		102	03JAN06A	24MAY06A	0																																							
+ Project Construction																																												
		540	05JUL06A	26DEC07	3,768,778																																							
+ Project Close-Out																																												
		69	27DEC07	02APR08	0																																							
+																																												
		2,124*	30APR02A	21FEB08	0																																							
130 Women's Gym Renovation																																												
+ Pre-Design/Programming																																												
		802	01MAR04A	25APR07	0																																							
+ Project Design																																												
		248	26APR07	16APR08	0																																							
+ Project DSA Review																																												
		155	24APR08	03DEC08	0																																							
+ Project Bid and Award																																												
		191	10DEC08	09SEP09	0																																							
+ Project Construction																																												
		235	16SEP09	18AUG10	34,000																																							
+ Project Close-Out																																												
		82	19AUG10	15DEC10	0																																							

Start Date 01AUG00  
 Finish Date 06JUL11  
 Data Date 31JAN07  
 Run Date 02MAR07 12:19

Early Bar  
 Progress Bar  
 Critical Activity


017U

LACCD  
 Los Angeles City College  
 Campus Summary




Sheet 8 of 18

Date	Revision	Checked	Approved

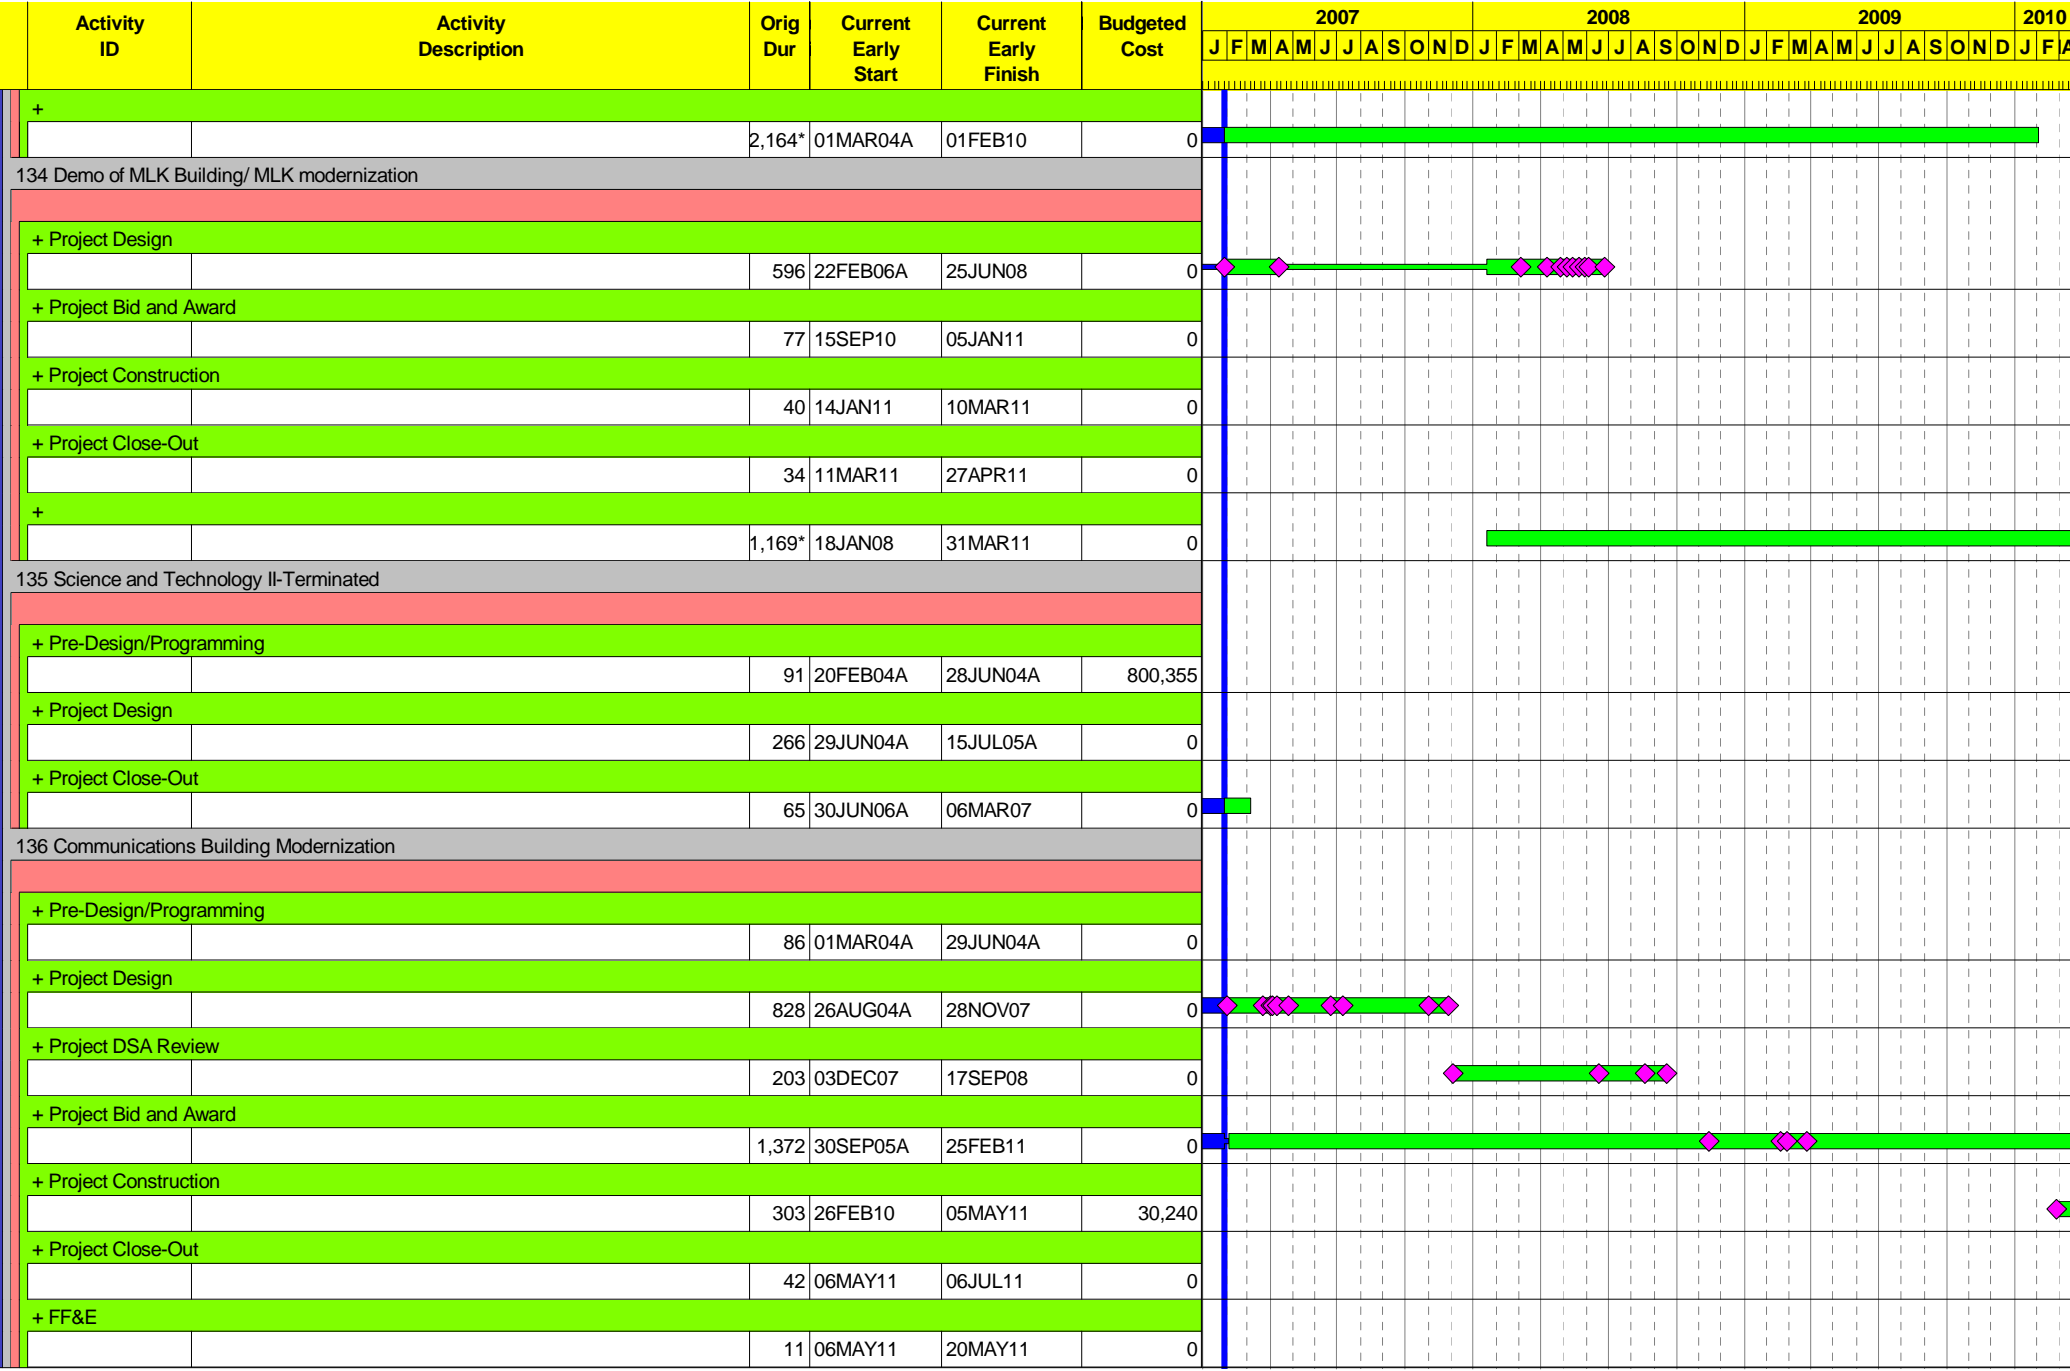



Start Date 01AUG00  
 Finish Date 06JUL11  
 Data Date 31JAN07  
 Run Date 02MAR07 12:19




 Early Bar  
 Progress Bar  
 Critical Activity

017U  
 LACCD  
 Los Angeles City College  
 Campus Summary

Date	Revision	Checked	Approved

Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010		
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A
+																																												
		2,651*	01MAR04A	03JUN11	0	[Green Bar]																																						
170 Master Planning																																												
+ Master Plan																																												
		217	01AUG01A	31MAY02A	606,016																																							
172 Emergency Lighting, Fire Alarm & Sec Systems																																												
+ Project Construction																																												
		1,871	22OCT03A	03MAR11	173,239	[Green Bar]																																						
+ Project Close-Out																																												
		1,786	26FEB04A	09MAR11	0	[Blue Bar]																																						
173 RWGPL																																												
173.01 RWGPL - Site Utilities Infrastructure																																												
+ Project Design																																												
		236	16AUG04A	20JUL05A	0																																							
+ Project Construction																																												
		1,413	16AUG04A	10MAR10	13,340,550	[Green Bar]																																						
+ Project Close-Out																																												
		40	11MAR10	05MAY10	0	[Green Bar]																																						
173.02 RWGPL - Landscaping Cntrl Wk and N. Quad																																												
+ Project Design																																												
		834	15JUN04A	26SEP07	0	[Green Bar]																																						
+ Project Bid and Award																																												
		84	02NOV09	03MAR10	0	[Green Bar]																																						
+ Project Construction																																												
		70	28DEC10	05APR11	90,000	[Green Bar]																																						
+ Project Close-Out																																												
		45	06APR11	08JUN11	0	[Green Bar]																																						
+																																												
		2,515*	15JUN04A	04MAY11	0	[Green Bar]																																						
173.03 RWGPL - Landscaping North Entry Plaza																																												
+ Project Design																																												
		873	15JUN04A	20NOV07	0	[Green Bar]																																						
+ Project DSA Review																																												
		160	21NOV07	09JUL08	0	[Green Bar]																																						
+ Project Bid and Award																																												
		94	17JUL08	26NOV08	0	[Green Bar]																																						

Start Date 01AUG00  
 Finish Date 06JUL11  
 Data Date 31JAN07  
 Run Date 02MAR07 12:19

 Early Bar  
 Progress Bar  
 Critical Activity

017U  
 LACCD  
 Los Angeles City College  
 Campus Summary

Sheet 11 of 18

Date	Revision	Checked	Approved

Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010		
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A
+ Project Construction																																												
+ Project Close-Out																																												
+																																												
173.04 RWGPL- Landscaping N. Gte & Wil. Brk Edge																																												
+ Project Design																																												
+ Project Bid and Award																																												
+ Project Construction																																												
+ Project Close-Out																																												
+																																												
173.05 RWGPL - Landscaping North of East Walk																																												
+ Project Design																																												
+ Project Bid and Award																																												
+ Project Construction																																												
+ Project Close-Out																																												
+																																												
173.06 RWGPL - Landscaping around Cafeteria																																												
+ Project Design																																												
+ Project Bid and Award																																												
+ Project Construction																																												
+ Project Close-Out																																												
+																																												

Start Date 01AUG00  
 Finish Date 06JUL11  
 Data Date 31JAN07  
 Run Date 02MAR07 12:19




Early Bar  
 Progress Bar  
 Critical Activity

017U  
 LACCD  
 Los Angeles City College  
 Campus Summary

Date	Revision	Checked	Approved

Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010		
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A
173.08 Replace Electrical at Chem Demolition																																												
+ Project Design																																												
		166	20SEP04A	13MAY05A	43,207																																							
174 Signage for Safety and Public Information																																												
+ Project Design																																												
		854	15JUN04A	24OCT07	0																																							
+ Project Bid and Award																																												
		54	16DEC09	03MAR10	0																																							
+ Project Construction																																												
		70	28DEC10	05APR11	80,818																																							
+ Project Close-Out																																												
		45	06APR11	08JUN11	0																																							
+																																												
		2,515*	15JUN04A	04MAY11	0																																							
175 Restrooms Modernization																																												
+ Project Design																																												
		284	01JUL02A	06AUG03A	0																																							
+ Project DSA Review																																												
		129	28MAY03A	25NOV03A	0																																							
+ Project Bid and Award																																												
		57	05DEC03A	25FEB04A	0																																							
+ Project Construction																																												
		681	15MAR04A	15NOV06A	1,190,039																																							
+ Project Close-Out																																												
		13	30OCT06A	15NOV06A	0																																							
+																																												
		1,599*	01JUL02A	15NOV06A	0																																							
176 Demolition of Temp / Obsolete Facilities																																												
176.01 Demolition of Maintenance Bungalows																																												
+ Project Design																																												
		53	16OCT02A	30DEC02A	0																																							
+ Project Construction																																												
		6	23DEC02A	31DEC02A	118,475																																							
176.02 Demolition of Tennis Courts, Bungalows																																												
+ Project Construction																																												
		44	14APR03A	12JUN03A	258,628																																							

Start Date 01AUG00  
 Finish Date 06JUL11  
 Data Date 31JAN07  
 Run Date 02MAR07 12:19

 Early Bar  
 Progress Bar  
 Critical Activity

017U

LACCD  
 Los Angeles City College  
 Campus Summary

Sheet 13 of 18

Date	Revision	Checked	Approved










Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010		
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A
179.05 Campus Imprvmnts - Elec.Infrastructure																																												
+ Project Construction																																												
		1,157	30JUN06A	21JAN11	0	[Gantt bar from 30JUN06 to 21JAN11]																																						
+ Project Close-Out																																												
		33	24JAN11	09MAR11	0	[Gantt bar from 24JAN11 to 09MAR11]																																						
180 Site Survey and Infrastructure Studies																																												
+ Project Construction																																												
		1,324	03JUN02A	08AUG07	310,382	[Gantt bar from 03JUN02 to 08AUG07]																																						
+ Project Close-Out																																												
		44	09AUG07	10OCT07	0	[Gantt bar from 09AUG07 to 10OCT07]																																						
181 Environmental Impact Report (EIR)																																												
+ EIR / CEQA																																												
		1,295	10JAN02A	02FEB07	287,605	[Gantt bar from 10JAN02 to 02FEB07]																																						
182 CEQA																																												
+ EIR / CEQA																																												
		1	29NOV02A	29NOV02A	47	[Gantt bar from 29NOV02 to 29NOV02]																																						
189 Asset Assessment and Move Management																																												
+ Project Construction																																												
		2,338	01JAN02A	04MAR11	2,018,291	[Gantt bar from 01JAN02 to 04MAR11]																																						
190 Program Management																																												
+ Program / Project Management																																												
		2,338	01JAN02A	04MAR11	2,252,494	[Gantt bar from 01JAN02 to 04MAR11]																																						
191 Project Management																																												
+ Program / Project Management																																												
		2,787	05AUG00A	06JUL11	14,867,545	[Gantt bar from 05AUG00 to 06JUL11]																																						
192 Reimbursables																																												
+ Project Construction																																												
		153	05AUG00A	10MAR01A	0	[Gantt bar from 05AUG00 to 10MAR01]																																						
193 Legal Services																																												
+ Project Construction																																												
		2,338	01JAN02A	04MAR11	3,664,423	[Gantt bar from 01JAN02 to 04MAR11]																																						

Start Date 01AUG00  
 Finish Date 06JUL11  
 Data Date 31JAN07  
 Run Date 02MAR07 12:19

 Early Bar  
 Progress Bar  
 Critical Activity

017U  
 LACCD  
 Los Angeles City College  
 Campus Summary

Date	Revision	Checked	Approved

